



CERTIFICATE OF QUALITY

EverSure™ Type GP Cement

NZS3122:2009 (Bulk Despatch)



Our
NZ made
cement is
genuine
NZ grade
cement.

Issued to: National Sales Manager

Test Report No: 20#104

info@goldenbay.co.nz

Code	Week Ending / Voyage	Specific Surface Area	Normal Consistency	Initial Set	Final Set	Soundness	Compressive Strength						Free Lime	Sodium Equivalent (NaEq)	Sulphur Trioxide (SO3)	
							ISOCEN			Concrete						
							3 days	7 days	28 days	Slump	3 days	7 days				28 days
Mean		341	29.0	134	3:31	1	33.1	46.2	65.3	92.3	25.8	34.0	46.9	1.7	0.54	2.2
Standard Deviation		10	0.1	7	0:10	0.6	0.8	1.5	1.6	3.3	1.7	1.2	2.5	0.2	0.01	0.0
Min		320	28.8	120	3:15	0	31.5	43.2	63.0	90.0	22.7	32.3	43.8	1.4	0.52	2.1
Max		360	29.2	150	3:45	2	34.6	48.5	67.8	100.0	27.5	36.1	50.8	2.0	0.57	2.3
NZS 3122:2009 Requirements				45 min	6:00 max	5 max		35.0 min	45.0 min						0.6 max	3.5 max
Units		m2/kg	%	minutes	hrs:mins	mm	MPa	MPa	MPa	mm	MPa	MPa	MPa	%	%	%
200605-860-GP	05/06/20	360	29.0	135	3:30	1	34.1							1.7	0.55	2.2
200603-858-GP	3/06/20	340	29.1	135	3:30	1	32.6			90	26.8			1.9	0.52	2.2
200529-495-GP	29/05/20	350	29.1	135	3:30	1	33.1	45.3						1.6	0.55	2.2
200527-493-GP	27/05/20	340	28.9	135	3:30	2	33.1	46.7		90	27.9	36.1		1.7	0.55	2.2
200522-032-GP	22/05/20	340	28.8	120	3:15	1	34.4	47.3						1.7	0.56	2.1
200517-030-GP	17/05/20	350	28.9	135	3:30	2	32.9	46.6		90	26.4	32.4		2.0	0.54	2.1
200515-657-GP	15/05/20	335	28.9	150	3:45	0	32.4	43.2						1.7	0.56	2.3
200513-655-GP	13/05/20	335	28.8	150	3:30	1	33.1	46.0		95	25.9	35.3		1.6	0.53	2.2
200508-344-GP	08/05/20	325	28.9	135	3:45	2	32.6	44.7	65.5					1.7	0.55	2.3
200505-327-GP	05/05/20	345	28.8	135	3:30	1	32.8	44.5	63.9	90	27.1	34.6	47.1	2.0	0.52	2.2
200430-034-GP	30/04/20	345	28.9	135	3:30	0	32.5	44.3	65.1	100	22.7	33.2	44.2	2.0	0.53	2.3
200325-999-GP	25/03/20	345	29.2	135	3:30	0	32.9	45.8	65.2	90	26.6	34.2	47.6	2.0	0.55	2.2
200317-595-GP	17/03/20	350	29.2	135	3:15	0	33.3	46.0	64.0	90	27.5	35.0	46.8	2.0	0.53	2.2
200315-597-GP	15/03/20	345	29.2	135	3:15	0	33.8	48.4	65.3					1.8	0.55	2.1
200311-240-GP	11/03/20	355	29.2	120	3:15	1	34.3	48.3	66.0					1.7	0.56	2.3
200308-190-GP	08/03/20	340	29.2	135	3:45	1	33.1	48.1	63.0	90	26.5	34.5	48.9	1.8	0.54	2.1
200305-836-GP	05/03/20	335	29.0	135	3:45	1	32.4	46.9	65.0	95	25.2	32.3	48.9	1.7	0.57	2.2
200303-834-GP	03/03/20	355	29.0	135	3:30	1	34.6	48.5	63.4					1.6	0.54	2.2
200225-421-GP	25/02/20	340	29.0	135	3:45	1	34.0	47.2	63.6	90	26.6	33.7	50.8	1.6	0.55	2.1
200223-471-GP	23/02/20	330	28.9	120	3:15	1	33.6	46.5	63.2					1.8	0.55	2.2
200219-040-GP	19/02/20	340	29.0	135	3:45	1	34.0	48.0	67.3					1.4	0.55	2.2
200216-038-GP	16/02/20	340	28.9	135	3:45	1	32.5	45.4	67.0	95	23.2	33.3	44.2	1.7	0.55	2.2
200213-682-GP	13/02/20	325	28.9	135	3:30	1	32.1	45.0	67.3	95	23.3	32.7	43.8	1.6	0.53	2.2
200209-680-GP	09/02/20	330	28.8	135	3:30	1	32.4	45.3	67.1					1.7	0.53	2.2
200207-517-GP	07/02/20	320	28.8	135	3:30	2	31.5	45.1	67.8					1.7	0.54	2.2

This Report must not be reproduced except in full

The above samples were tested as received in accordance with the current terms of accreditation and methods stated in NZS 3122:2009 with the exception of:
Chemical composition to ASTM C114-18

- Concrete Compressive Strength test results outside the scope of accreditation

Sample tested @ 57 days
Sample tested @ 42 days
Sample tested @ 50 days
No result available at time of certificate issue

Handwritten signature



Portland Works, Portland, Whangarei 0178

Jim White
Quality System Co-ordinator

Date issued: 12/06/2020

Page 1 of 3




**EverSure™
Type GP Cement**



**Compressive Strength ISO-CEN Mortar
(Bulk Despatch)**

—x— 28 Days —■— 7 Days —◆— 3 Days

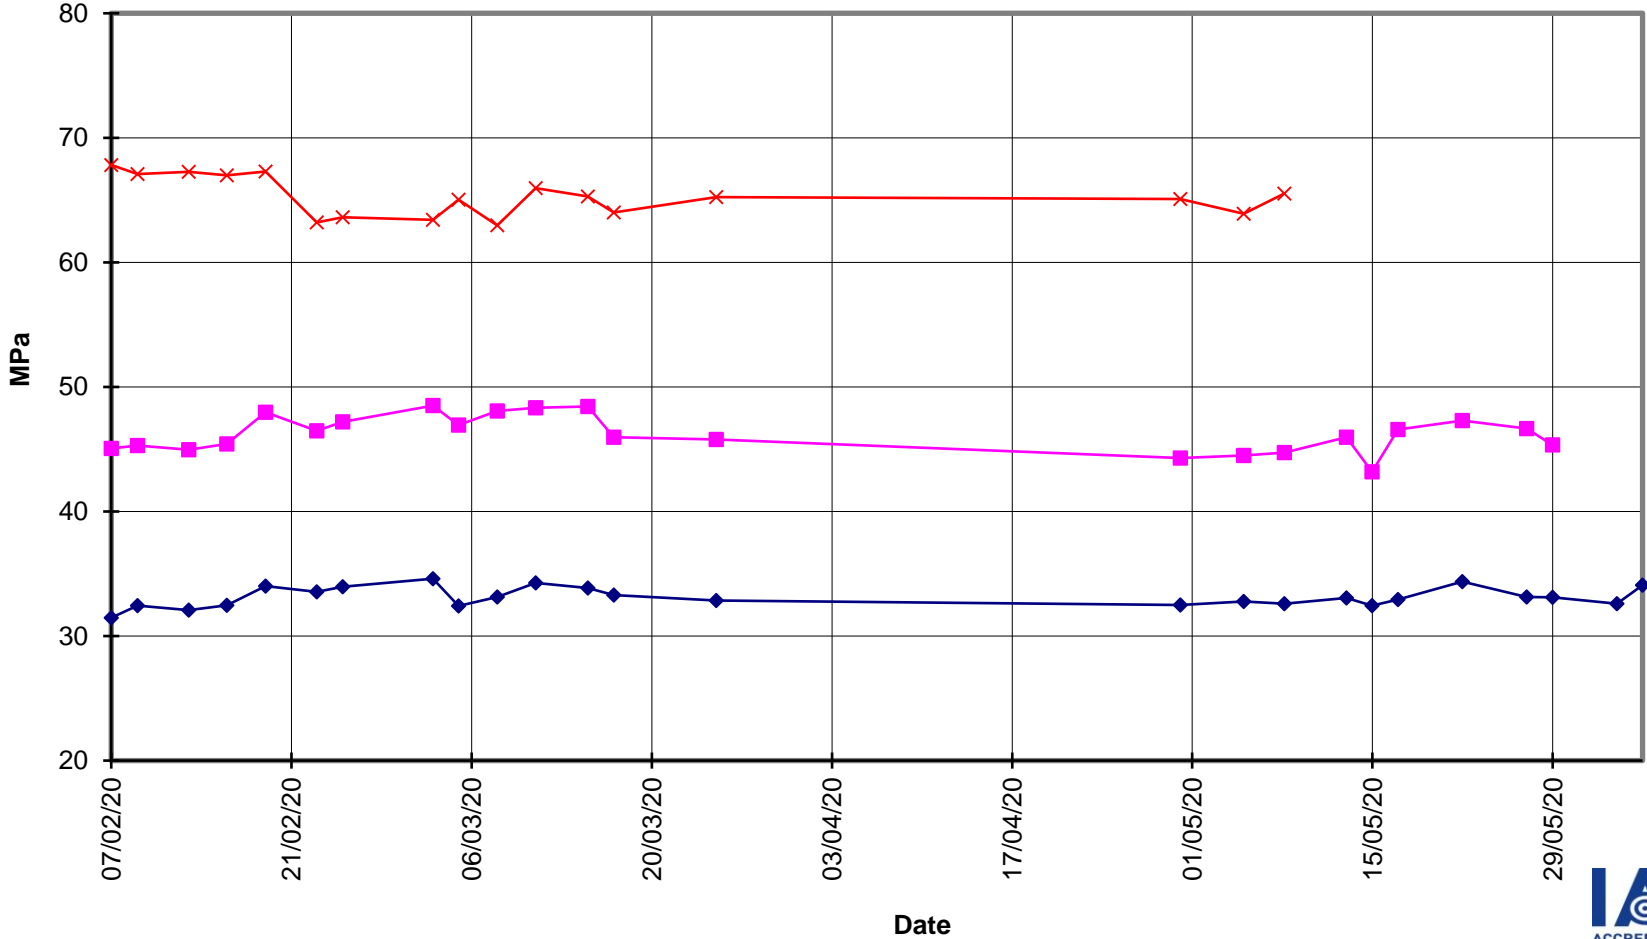



**EverSure™
Type GP Cement**

**Compressive Strength Concrete
(Bulk Despatch)**



—x— 28 Days —■— 7 Days —◆— 3 Days —■— Slump

